

Panther Grove 2

	11-Sep-26	Today
Daily Weather as of 7:00am	0	0
Low Temperature (F)	64	67
High Temperature (F)	81	85
Ground Wind Speed (MPH):	8 MPH	8 MPH
Precipitation (in)	0.00	15%
August Precip Total (in)	0.00	

	ACTIVITY
Public Roads	Strip Public Road Radii
	Mowing Public Road Radii
	Stone Public Road Radii
Access Roads	Strip Access Road
	Cement Stabilization
	Stone Access Road
	Strip Access Road Radii
	Stone Access Road Radii

LAST WORKING DAY
Friday, September 11, 2026
LOCATION(S)
P4 (IL 116-CH 13)
P20 (CH 8-400E RD)
Substation
T86, T92
T92

Daily Safety Topics

Driving to work areas- Always follow site speed limits, come to a complete stop at all stop signs, look both ways and be aware of cross traffic, pedestrians, and locals, avoid distractions, wear your seatbelt, maintain a safe following distance, Drive defensively.

Effective Communication- Speak up if you identify a hazard, unsafe condition, or potential risk. Actively participate in pre-task planning meetings and toolbox talks to ensure everyone understands the work scope and associated hazards. Communicate any changes in work conditions immediately to supervisors and affected crews. If you are unsure about a task, procedure, or instruction,

Site Notes

Saturday, September 12, 2026

TODAY
Saturday, September 12, 2026
LOCATION(S)


NEXT WORKING DAY
Tuesday, September 15, 2026
LOCATION(S)
P4 (IL 116-CH 13)
P4 (IL 116-CH 13)



Quantity Tracking				
QTY LAST WORKDAY	QTY TO DATE	UNIT	TOTAL QTY	% COMPLETE
	7	EA	35	20.0%
	5	EA	35	14.3%
	49162	LF	161120	30.5%
	39423	LF	161120	24.5%
	29065	LF	161120	18.0%
	36	EA	TBD	#VALUE!
	29	EA	TBD	#VALUE!

Site Information	
Manpower	
4	White Construction Management
14	White Construction Operators
12	White Construction Laborers
	White Construction Ironworkers
	White Construction Millwright
	White Construction Electrician
	Dunn Company
	West Wind
	Tobey's Construction & Cartage
	KVCC
30	Total
Equipment	
10	Pickup Trucks
2	Dozers
2	Rollers
2	Graders
2	Cargo Trailer
0	Cranes
1	Excavators
0	Forklift
3	Trailers
1	Sand Truck
2	Sheepfoot Roller
2	Reclaimer Stabilizer
2	Smooth Drum Roller
3	Water Trucks
2	Skid Steer
34	Total

Additional Comments

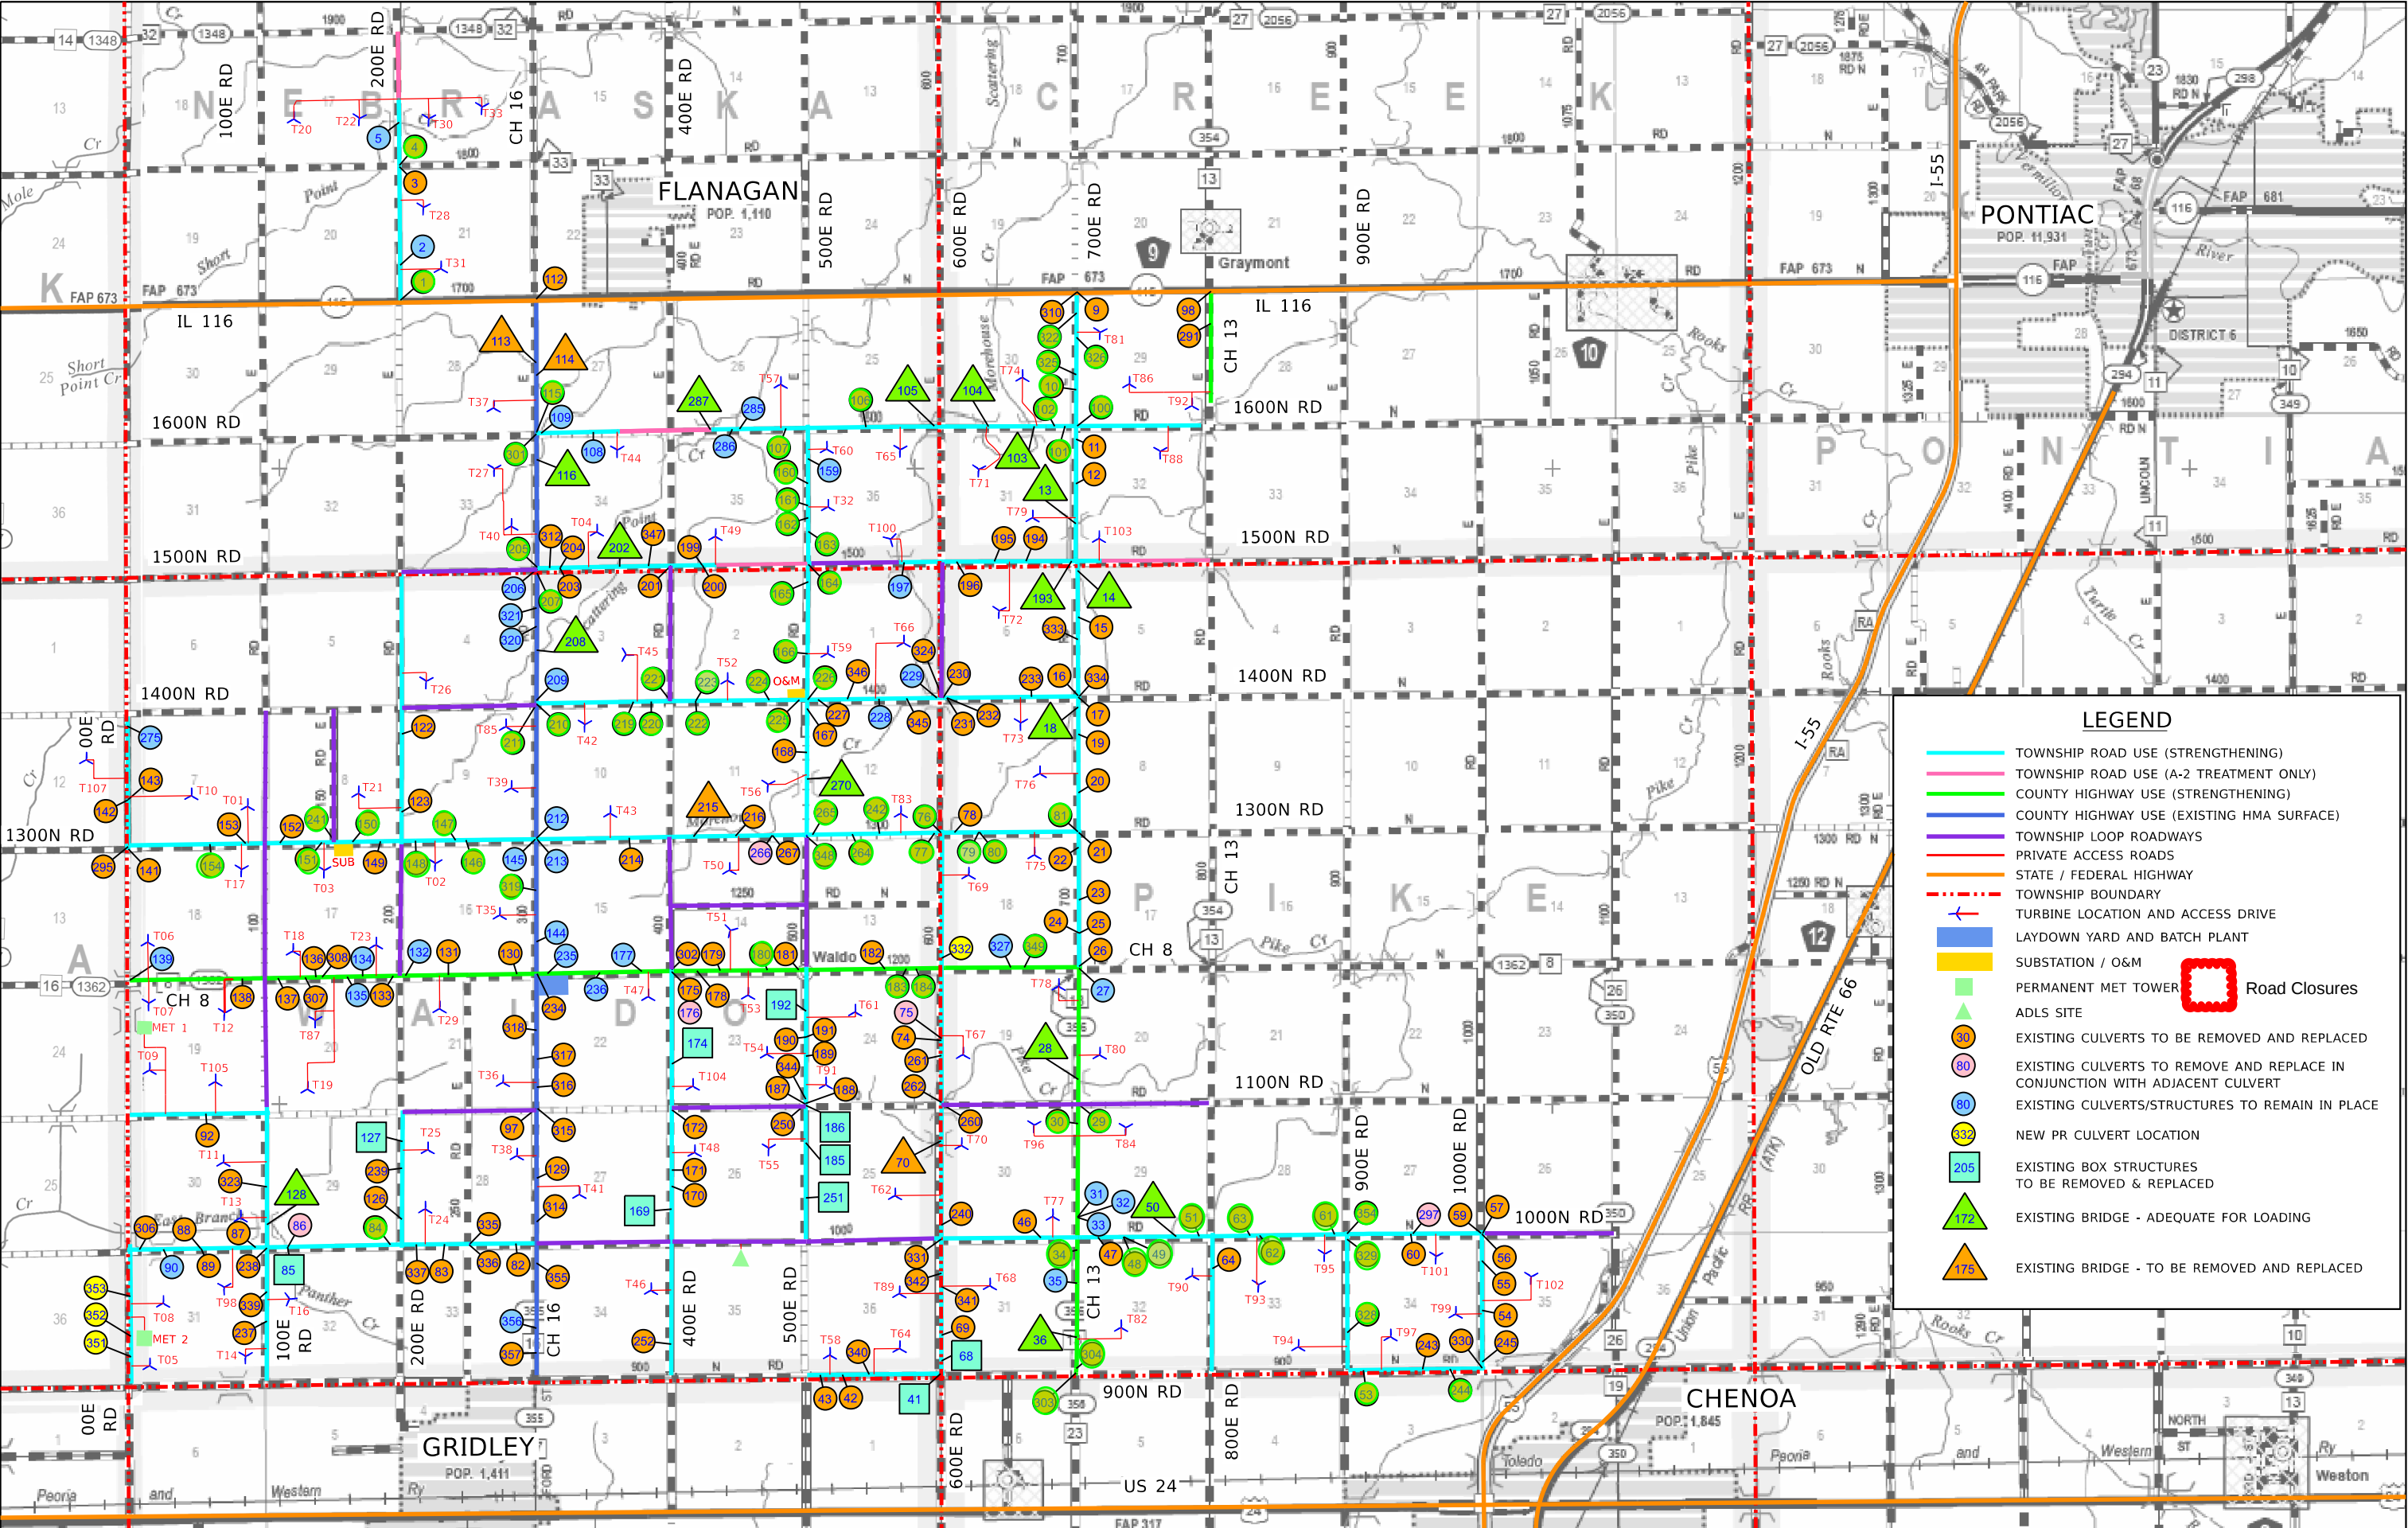

LEGEND

- TOWNSHIP ROAD USE (STRENGTHENING)
- TOWNSHIP ROAD USE (A-2 TREATMENT ONLY)
- COUNTY HIGHWAY USE (STRENGTHENING)
- COUNTY HIGHWAY USE (EXISTING HMA SURFACE)
- TOWNSHIP LOOP ROADWAYS
- PRIVATE ACCESS ROADS
- STATE / FEDERAL HIGHWAY
- TOWNSHIP BOUNDARY
- TURBINE LOCATION AND ACCESS DRIVE
- LAYDOWN YARD AND BATCH PLANT
- SUBSTATION / O&M
- PERMANENT MET TOWER
- ADLS SITE
- EXISTING CULVERTS TO BE REMOVED AND REPLACED
- EXISTING CULVERTS TO REMOVE AND REPLACE IN CONJUNCTION WITH ADJACENT CULVERT
- EXISTING CULVERTS/STRUCTURES TO REMAIN IN PLACE
- NEW PR CULVERT LOCATION
- EXISTING BOX STRUCTURES TO BE REMOVED & REPLACED
- EXISTING BRIDGE - ADEQUATE FOR LOADING
- EXISTING BRIDGE - TO BE REMOVED AND REPLACED
- Road Closures

